

SERVICES. RESOURCES. COMMUNITY.

News *from the* City of Berkeley

Measure T1 Quarterly Update - December

City of Berkeley sent this bulletin at 12/16/2024 11:52 AM PST

December 16, 2024

[View this message as a webpage](#)



Funding for improvements to
City infrastructure and facilities.


City of Berkeley

T1 Bond, Phase 2 Project Updates

We are using funding from T1 bonds to improve sidewalks, storm drains, streets, parks, community centers, and other key infrastructure and facilities.

Measure T1 provides \$100 million of funding from bond revenue to pay for improvements to City infrastructure and facilities. Phase 1 projects are complete. This is an update on Phase 2 projects.

Get an overview of [Phase Two selected projects](#).

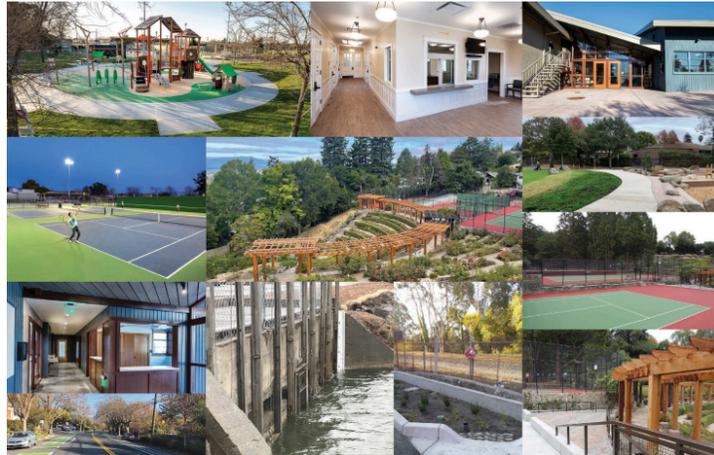

Measure T1 Capital Projects

Willard Park Clubhouse & Restroom Replacement Project



Willard Park New Restroom in Construction



Willard Clubhouse in Construction

Willard Clubhouse and Restroom project is in construction and expected to be completed in 2025.

African American Holistic Resource Center



African American Holistic Resource Center Conceptual Design

Forwarded this message from a friend?
[Click here to subscribe](#)

Sidewalk Repair Project



Prince St Sidewalk Repair Before and After Photo



King St Sidewalk Repair Before and After Photo

Sidewalk Repair Project is completed and in the close out phase. This project includes about **575** locations.

Restroom in the ROW - Telegraph/Channing



This Portland Loo style restroom will be located at Channing and Telegraph, expected completion in June 2025. This is one of 3 ROW Restrooms. The other two will be located at University/San Pablo and Alcatraz/Adeline

Projects in Construction or Out to Bid

Projects in Construction

- D & E Docks Replacement Project
- Willard Clubhouse & Restroom Replacement Project
- Ohlone Park Lighting and Restroom Project
- Telegraph/ Channing Restroom in the Right of Way

Projects Bidding for Construction

- Fire Station #2 - currently bidding
- CY-Green Room & Building H - will be going out to bid early 2025

D & E Docks Replacement Project

In water demolition of docks were completed by November 2024. Construction of new docks and landside will begin June 2025.



D & E Docks Replacement Demo photo



D&E Docks Replacement Pilings

T1 Phase 2 Project Updates

Facilities/Buildings

- **African American Holistic Resource Center Project** – In conceptual design phase, preparing zoning package.
- **MLK Jr. Youth Services Center** – Plans submitted for building permit review. Anticipate bidding in early 2025 and starting construction in Summer 2025.
- **Willard Park Clubhouse** – In construction.
- **SBSC – In design phase, preparing for community meetings and drawings for building permits in Spring 2025.**
- **Fire Station No. 2** – Advertised for public bid in December 2024, anticipated construction in Spring/Summer 2025 following award and contract execution.
- **Fire Station No. 6** –Project on hold after funding reallocated. Funding returning next year.
- **1947 Center Street Improvements** –The design complete and the structural alteration permit has been submitted to the building department for review.
- **PW Corporation Yard Improvements:**
 - **Green Room & Building H** – Design and permitting phase complete. Will be advertised for public bid beginning of 2025.
 - **Wash Station** – Currently in contract execution phase. Anticipated construction in the beginning of 2025.

Restrooms

- **Telegraph/Channing** – PG&E scope completed in October 2024. The Contractor has mobilized, and project estimated completion is expected by February 2025.
- **Adeline/Alcatraz** – Currently under PG&E design, with completion expected in March 2025.
- **San Pablo/University** – Design completed. Currently working on securing an encroachment permit with Caltrans.
- **Telegraph-Channing Parking Garage Restrooms & Elevators** – Currently in contract execution phase. Anticipated construction in Spring 2025.
- **Harrison Park Restroom** – In conceptual design.
- **Cesar Chavez Restroom on Spinnaker** – Site location directly on Spinnaker Way where existing port-a-potty and ADA parking spaces are located has been selected. A self-cleaning restroom is being pursued. A second community meeting was held on October 30, 2024. Currently the project is moving forward from conceptual design to the formal design process. Pre-Construction work to bring underground utilities to the project site before construction starts. Construction is expected to start in 2025.
- **Ohlone Park Restroom** – Design complete, construction contract awarded. Project in pre-construction phase. Construction to commence in January 2025 but anticipating a long lead time for pre-fabricated restroom, on-site work will not start until Spring 2025.
- **Willard Park Restroom** – In construction.
- **K Dock Restroom** – Construction is expected to start in 2025. Plans have been developed and the project is in the permitting phase.

Parks

- **John Hinkel Park** – Playground and Amphitheater Improvements were completed and celebrated on July 16, 2022.
- **King Pool Tile and Plaster Replacement** – Construction completed, and pool is open.
- **Grove Park Field and Playground Renovation Project**– Playground renovations were completed and celebrated on March 6, 2024. Field renovations were completed and celebrated on May 16, 2024.
- **Civic Center Park Upper Plaza Improvements** – Design complete, construction contract awarded. Project in pre-construction phase. Construction at the plaza to commence in January 2025.
- **Ohlone Park (East) Playground Replacement and Site Improvements** –Renovations were completed, and re-opening was celebrated on September 23, 2023.
- **Ohlone Park Lighting** – Design complete, construction contract awarded. Project in pre-construction phase. Construction to commence in January 2025, but anticipating a long lead time for materials, on-site work may not start until Spring 2025.
- **Aquatic Park Tide Tubes Clean Out** – Soil Removal: Phase 1B project is completed.

- **Tom Bates Sports Complex Restroom/Community Space** – Project is in the final design phase. The CEQA public review period of the Initial Study - Mitigated Negative Declaration has also been completed and currently working on addressing comments. Project will advertise in early Spring 2025 and anticipated to start construction in the Summer of 2025.

Waterfront

- **Replacement of Docks D & E at the Berkeley Marina** – First Phase of Construction (in-water demolition of docks) began in late September and completed by November 2024. Construction of new docks and landside improvements will resume in June 2025 and anticipated to be completed by January 2026.
- **Marina Pilings Replacement** – Project completed.

Streets/Storm/Pathways

- **Streets** – On Hold
- **FY22 Sidewalk Repair Project** –Currently in closeout, change orders and final retention pending.
- **Pathway Repairs** – part of Spec No. 23-11616-C (FY 23 Retaining Wall & Storm Drain Improvement Project). Construction executed. Expected start January 2025.
- **Bollard Conversion to Landscaping** – In design. Target for bid in February 2024. Construction expected to begin in Summer/Fall 2025.
- **Storm Improvements** – Construction completed at John Hinkel Park, Marin, Euclid, Spruce, Grizzly Peak, San Benito, High Court and Virginia.

Follow @cityofberkeley

[Emergency notifications](#)

[Emergency map](#)

[Manage my subscriptions](#) * [Unsubscribe from this list](#)

You are receiving this message because you are signed up to receive PRW Measure T1 Quarterly Update emails from the City of Berkeley. For questions, contact communications@berkeleyca.gov.

Subscribe to updates from City of Berkeley

Email Address e.g. name@example.com

Share Bulletin



Powered by



[Privacy Policy](#) | [Cookie Statement](#) | [Help](#)
