


Berkeley Southside Complete Streets Project

Facilities, Infrastructure, Transportation, Environment & Sustainability
Policy Committee


March 19, 2025



Project Location

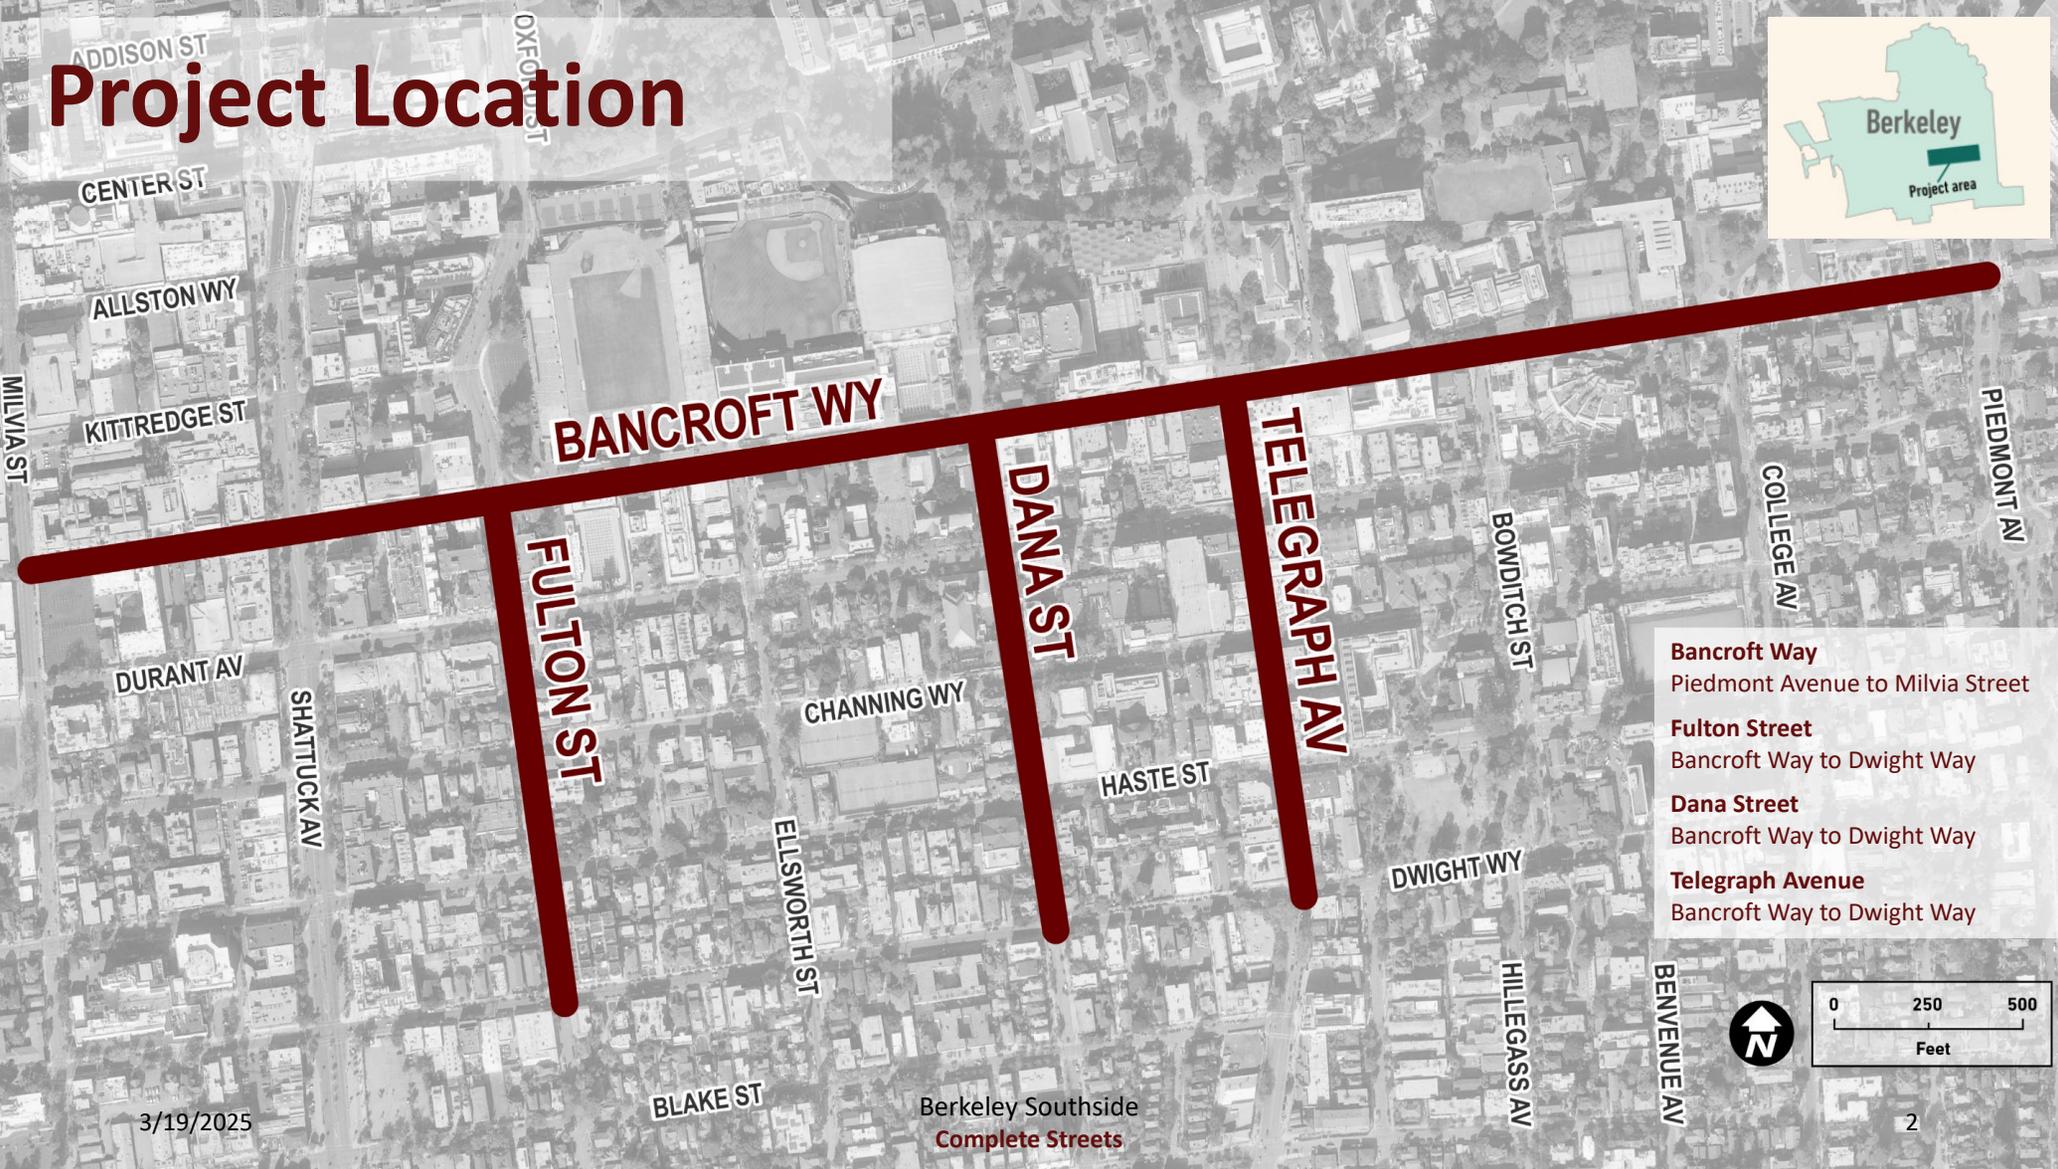

- Bancroft Way**
Piedmont Avenue to Milvia Street
- Fulton Street**
Bancroft Way to Dwight Way
- Dana Street**
Bancroft Way to Dwight Way
- Telegraph Avenue**
Bancroft Way to Dwight Way




3/19/2025

Berkeley Southside
Complete Streets

Project Goals


- **Safety** for all persons walking, riding bicycles, riding transit, or driving, consistent with the City of Berkeley Vision Zero traffic safety policy
- **Transit** reliability and travel times consistent with the City of Berkeley General Plan Transportation Element Policy T-4 “Transit-First”
- **Economic and cultural vitality** of Berkeley’s Southside neighborhood consistent with the Economic Development goals of the City of Berkeley Southside Plan

Project Timeline

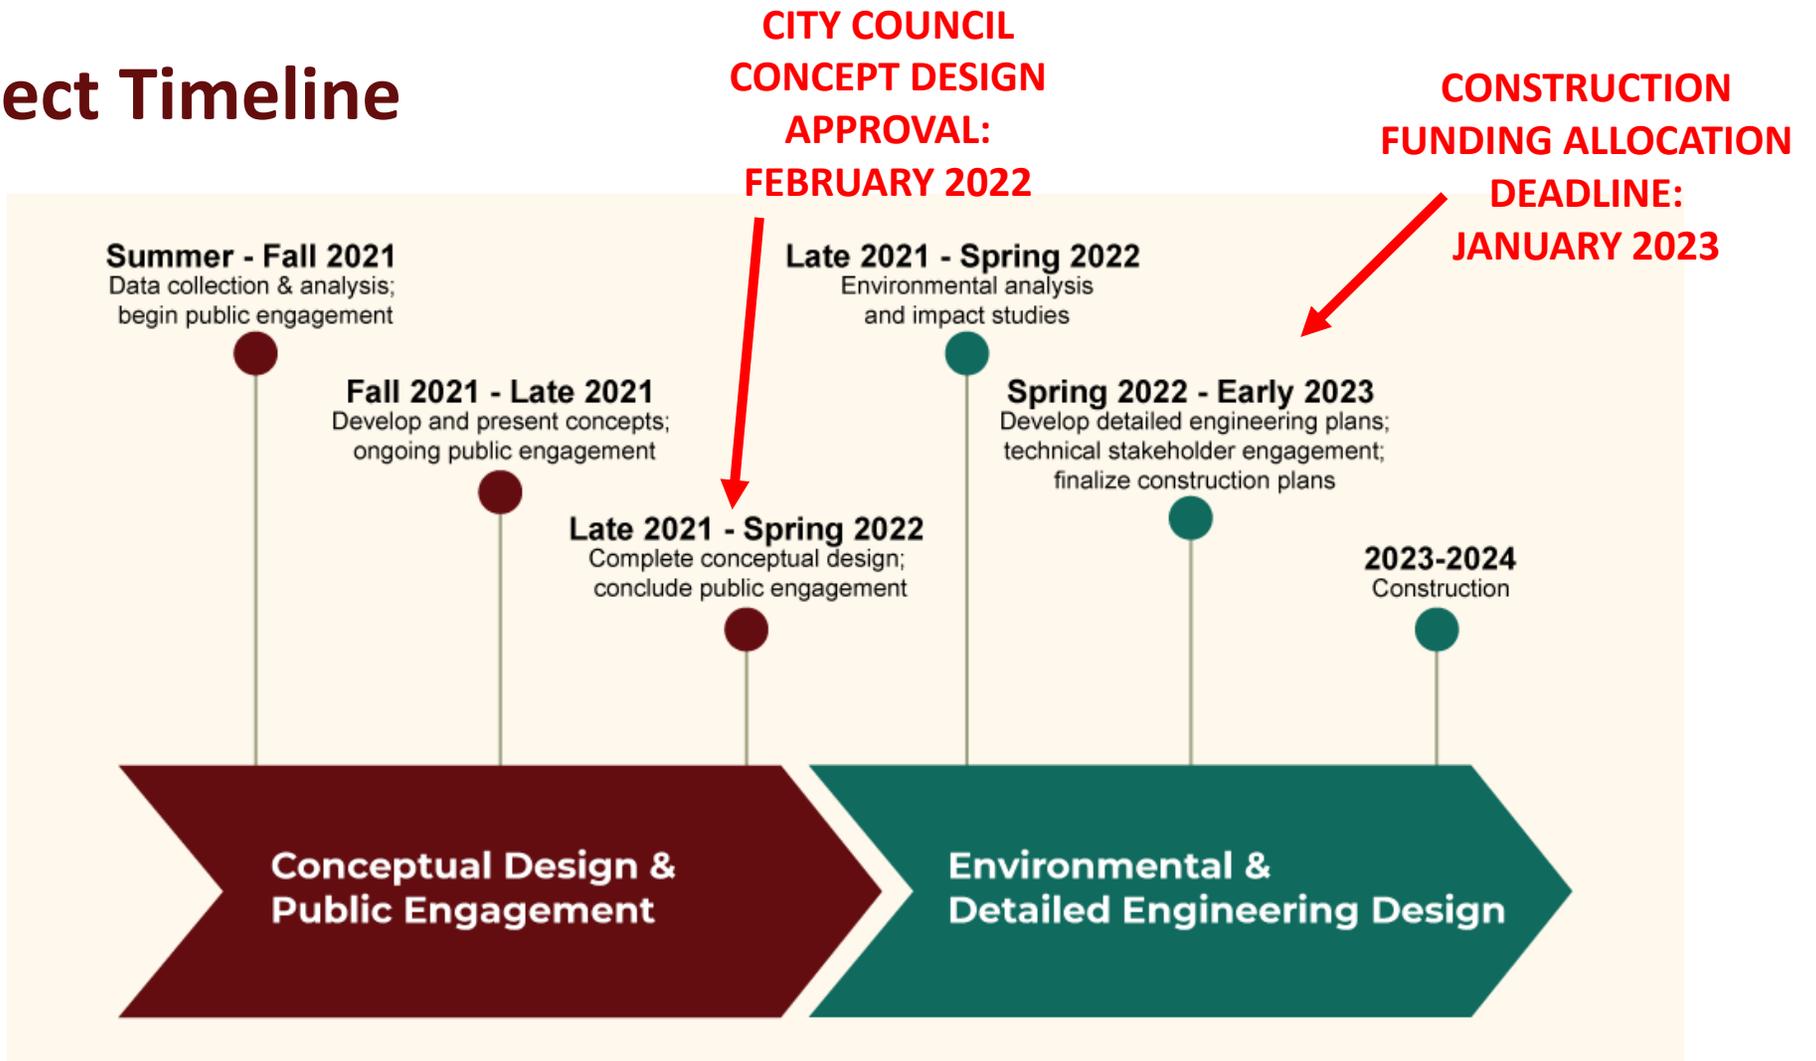


Construction Timeline Summary

- **Construction start: December 2023**
- **Storm Drain Improvements: Completed January 2024**
- **Concrete Work (curbs, islands, bus pads, etc...): Completed June 2024**
- **Pavement Reconstruction: Completed July 2024**
- **Curb paint, striping, green thermoplastic, and red transit paint: Completed August 2024**
- **Signal Work (on-going):**
 - All new signals installed and tested as of February 20, 2025
 - Final signal timing: on-going
 - New signals at Barrow Lane to be switched on once signal timing work is complete.

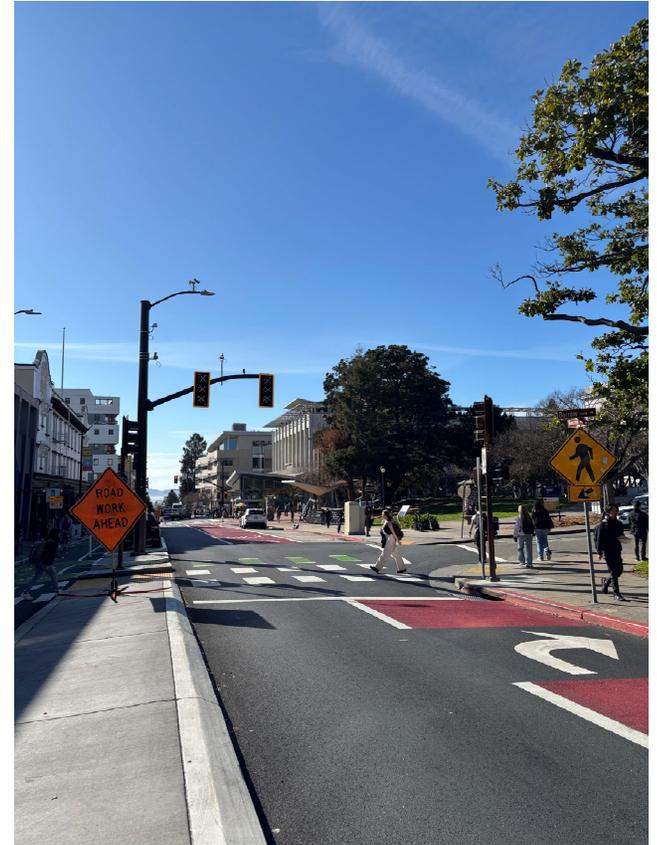

Outstanding Items


- **Signal Timing**
 - Staff reported issues with off-peak/mid-day signal timing along Bancroft Way
 - Transportation and the consultant team working on revised signal timing/phasing work.
 - Coordination with AC Transit traffic signal improvements.
 - Telegraph Avenue Rapid Corridors Project
 - Dana Complete Street Pilot Project
 - City electricians to test phasing and implement signal timing updates once final phasing is complete.
 - Work expected to be completed in approximately 1 month.
- **Detection zone camera aiming work**
 - Scheduled for the week beginning March 31.
 - Include consideration for detection of cyclists at protected advanced waiting areas.

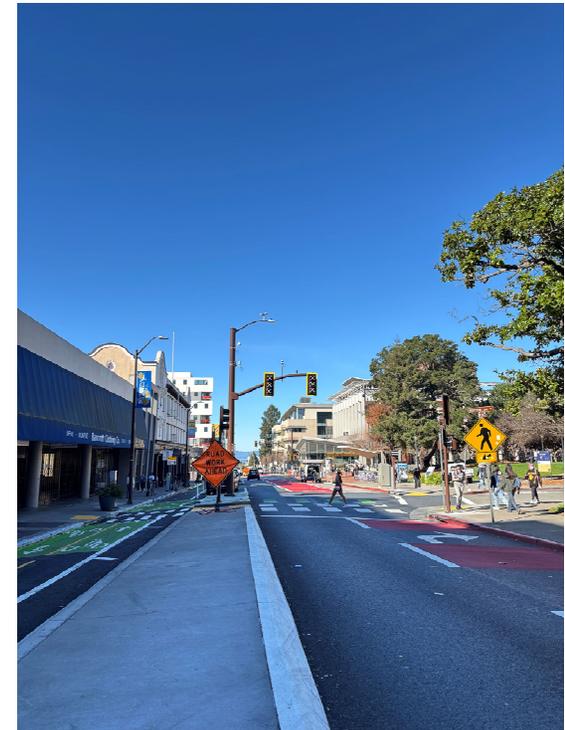

Bancroft Way looking west to new signal at Barrow Lane

Outstanding Items

- Planter bollard south of Fulton and Dwight
 - Restricting right turns onto Fulton Way for eastbound Dwight traffic
 - Team working on relocating bollard and adding signage to restrict right turn on reds to improve safety of bicyclists.

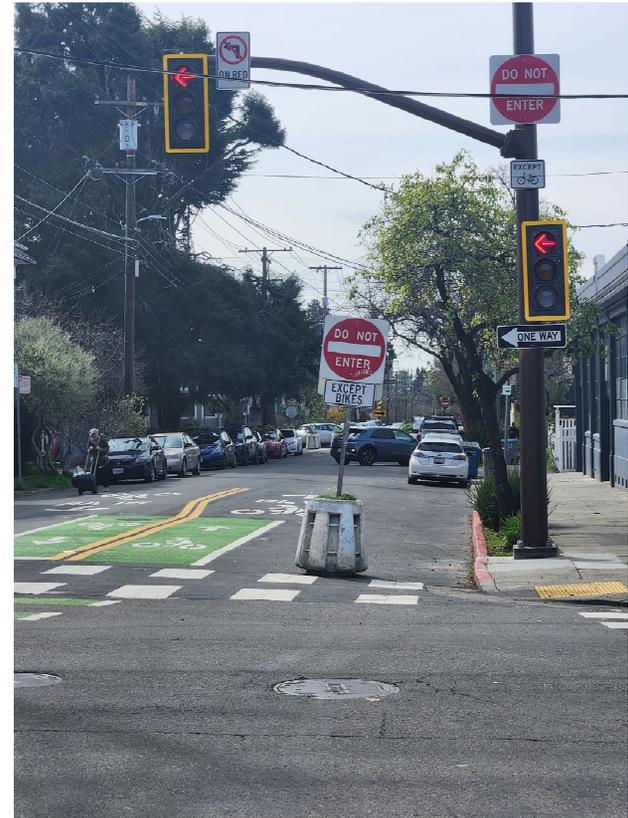

Fulton Way at Dwight Way looking south

Post Construction Photos



Bancroft Way (looking west toward Fulton Street)



Bancroft Way (looking west toward Fulton Street)

Post Construction Photos



Bancroft Way at Dana Street (looking east)



Bancroft Way (looking west between Dana Street and Sather Lane)

3/19/2025

Berkeley Southside
Complete Streets

Post Construction Photos



Bancroft Way at Barrow Lane (looking east)



Bancroft Way (looking east at Bowditch Street intersection)

Thank You!

More questions or comments?

Please contact

Ricardo Salcedo at

rsalcedo@berkeleyca.gov

